
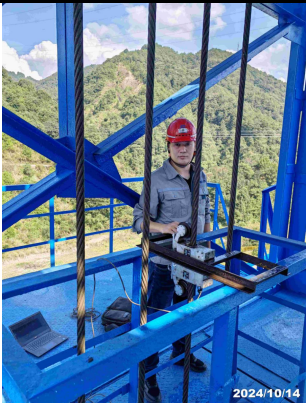
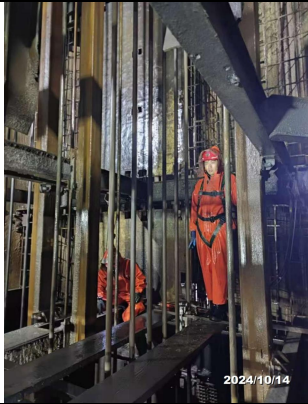


序号	报告编号	发布时间	结论	影像资料
1	GX-B1547/20-2-24023~24026	2024/11/1	所检项目合格	
2	GX-B1547/20-2-24027~24029	2024/11/1	所检项目合格	

3	GX-B1598/24-2-24249	2024/11/6	实测钢丝绳有效截面积损失百分比最大为1.85%，小于5%为正常。	
4	GX-B1598/24-2-24250	2024/11/6	实测钢丝绳有效截面积损失百分比最大为2.04%，小于5%为正常。	

5	GX-B1598/24-2-24251	2024/11/6	实测钢丝绳有效截面积损失百分比最大为1.68%，小于5%为正常。			
6	GX-B1598/24-2-24252	2024/11/6	实测钢丝绳有效截面积损失百分比最大为1.79%，小于5%为正常。			

7	GX-B1598/24-2-24253	2024/11/6	实测钢丝绳有效截面积损失百分比最大为0.98%，小于5%为正常。			
8	GX-B1598/24-2-24254	2024/11/6	实测钢丝绳有效截面积损失百分比最大为1.16%，小于5%为正常。			

9	GX-B1598/24-2-24255	2024/11/6	实测钢丝绳有效截面积损失百分比最大为1.04%，小于5%为正常。	 2024/10/14
10	GX-B1598/24-2-24256	2024/11/6	实测钢丝绳有效截面积损失百分比最大为0.94%，小于5%为正常。	 2024/10/14

11	GX-B1598/24-2-24257	2024/11/6	实测钢丝绳有效截面积损失百分比最大为1.27%，小于5%为正常。	 A worker in an orange safety suit is performing maintenance on a steel structure. The worker is standing on a platform and is using a tool to inspect or adjust a component. The date 2024/10/14 is visible in the bottom right corner of the image.
12	GX-B1598/24-2-24258	2024/11/6	实测钢丝绳有效截面积损失百分比最大为1.55%，小于5%为正常。	 A worker in an orange safety suit is performing maintenance on a steel structure. The worker is standing on a platform and is using a tool to inspect or adjust a component. The date 2024/10/14 is visible in the bottom right corner of the image.

13	GX-B1598/24-2-24259	2024/11/7	实测钢丝绳有效截面积损失百分比最大为1.59%，小于5%为正常。			
14	GX-B1598/24-2-24260	2024/11/7	实测钢丝绳有效截面积损失百分比最大为1.28%，小于5%为正常。			



15	GX-B1598/24-2-24261	2024/11/7	实测钢丝绳有效截面积损失百分比最大为1.66%，小于5%为正常。			
16	GX-B1598/24-2-24262	2024/11/7	实测钢丝绳有效截面积损失百分比最大为1.87%，小于5%为正常。			



17	GX-B1598/24-2-24263	2024/11/7	实测钢丝绳有效截面积损失百分比最大为0.73%，小于5%为正常。			
18	GX-B1598/24-2-24264	2024/11/7	实测钢丝绳有效截面积损失百分比最大为0.64%，小于5%为正常。			

19	GX-B1598/24-2-24265	2024/11/7	实测钢丝绳有效截面积损失百分比最大为0.70%，小于5%为正常。			
20	GX-B1598/24-2-24266	2024/11/7	实测钢丝绳有效截面积损失百分比最大为0.84%，小于5%为正常。			

21	GX-B1302/23-2-24007	2024/11/6	综合判定：合格。	
----	---------------------	-----------	----------	---
